


ABATEMENT AND DEMOLITION FLOWCHART


Office of Environmental Services
December 2000

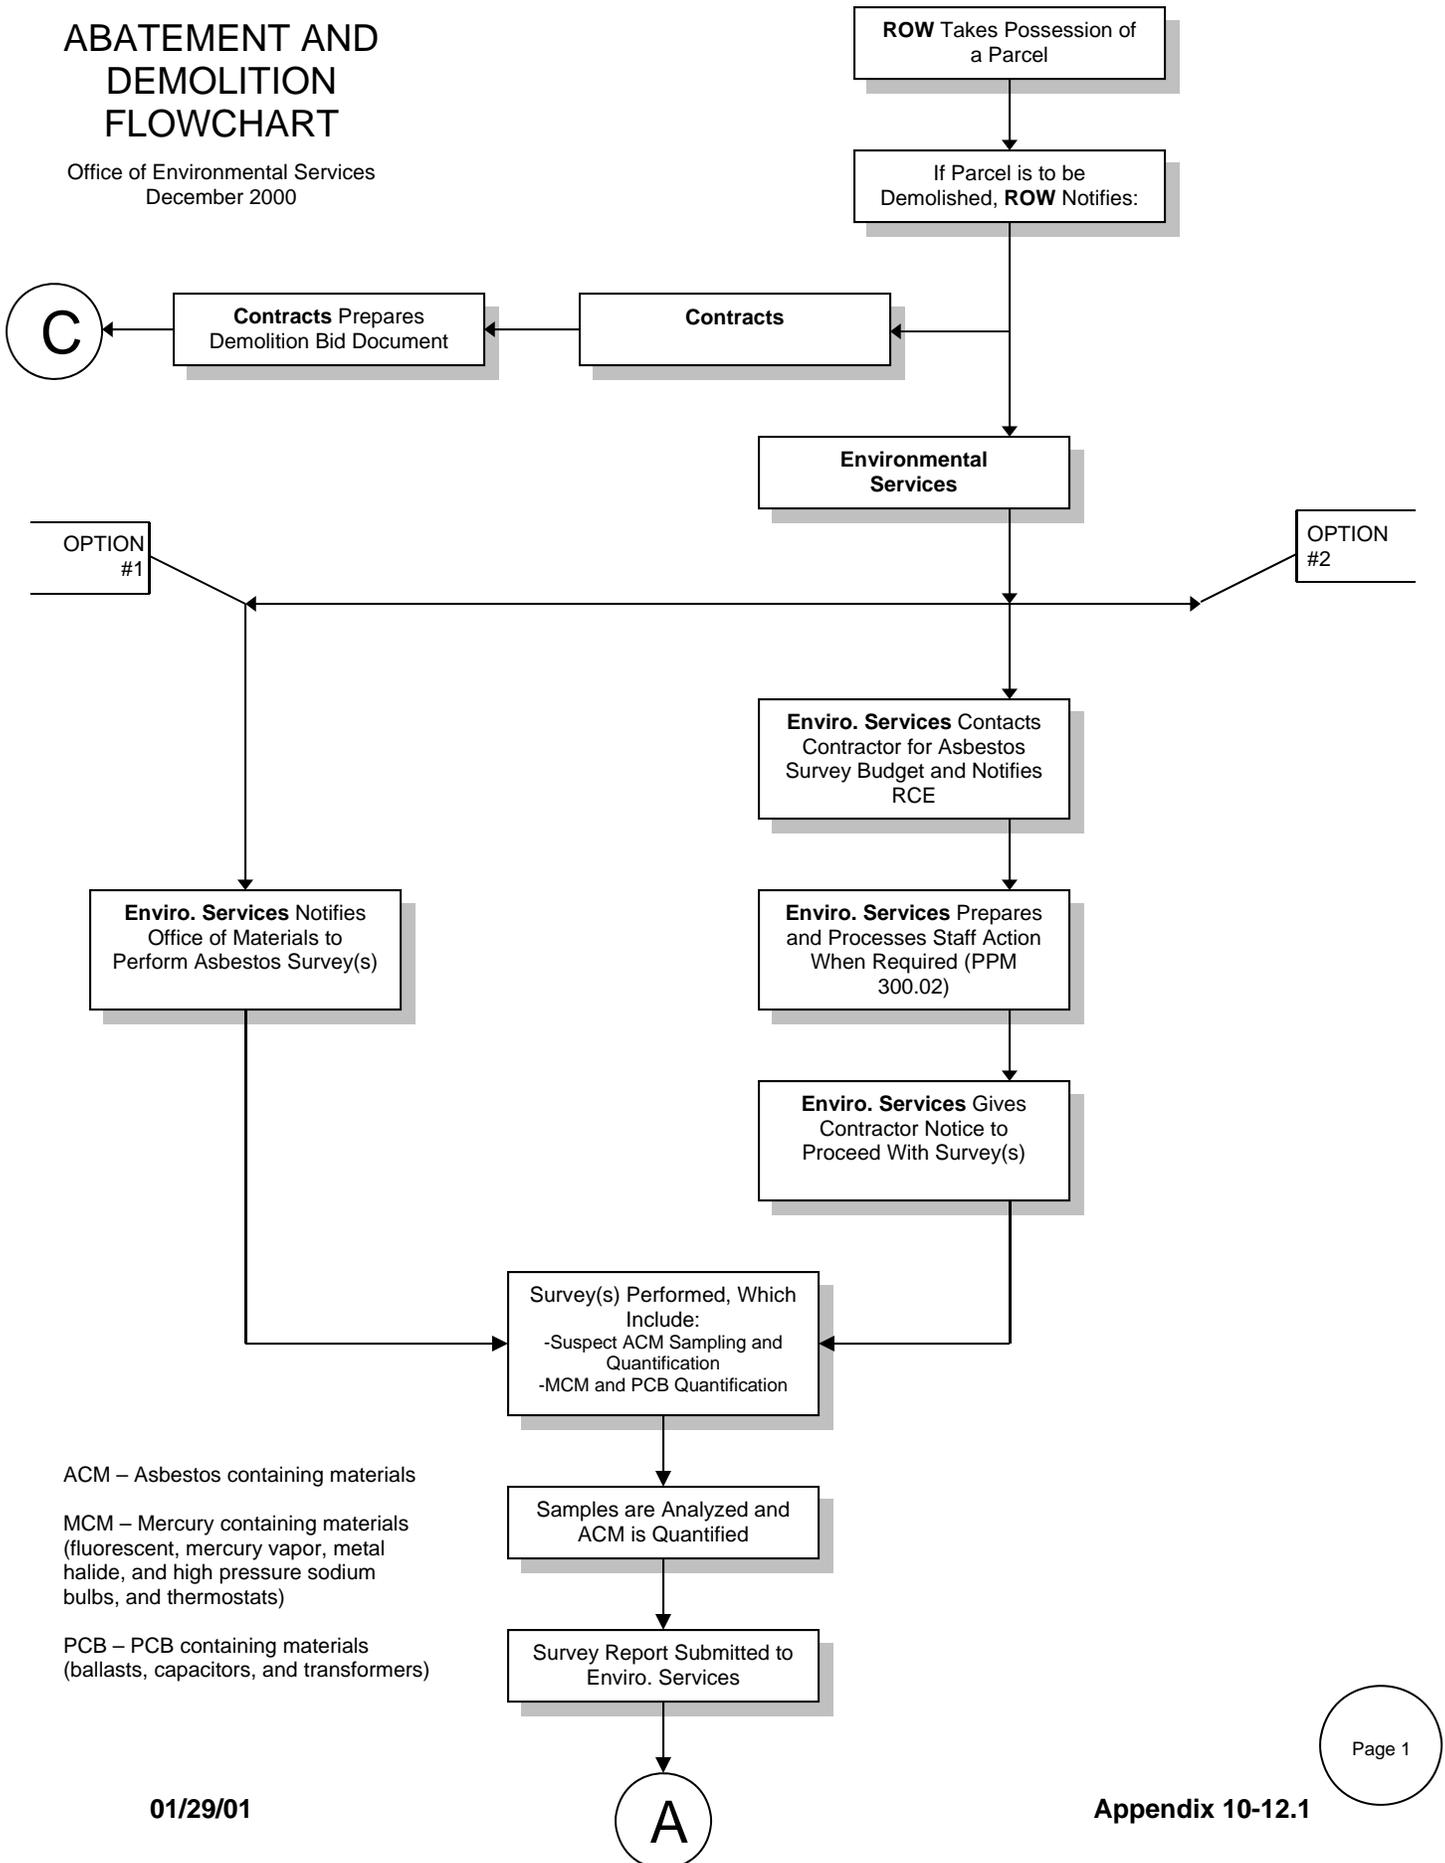


ACM – Asbestos containing materials

MCM – Mercury containing materials (fluorescent, mercury vapor, metal halide, and high pressure sodium bulbs, and thermostats)

PCB – PCB containing materials (ballasts, capacitors, and transformers)

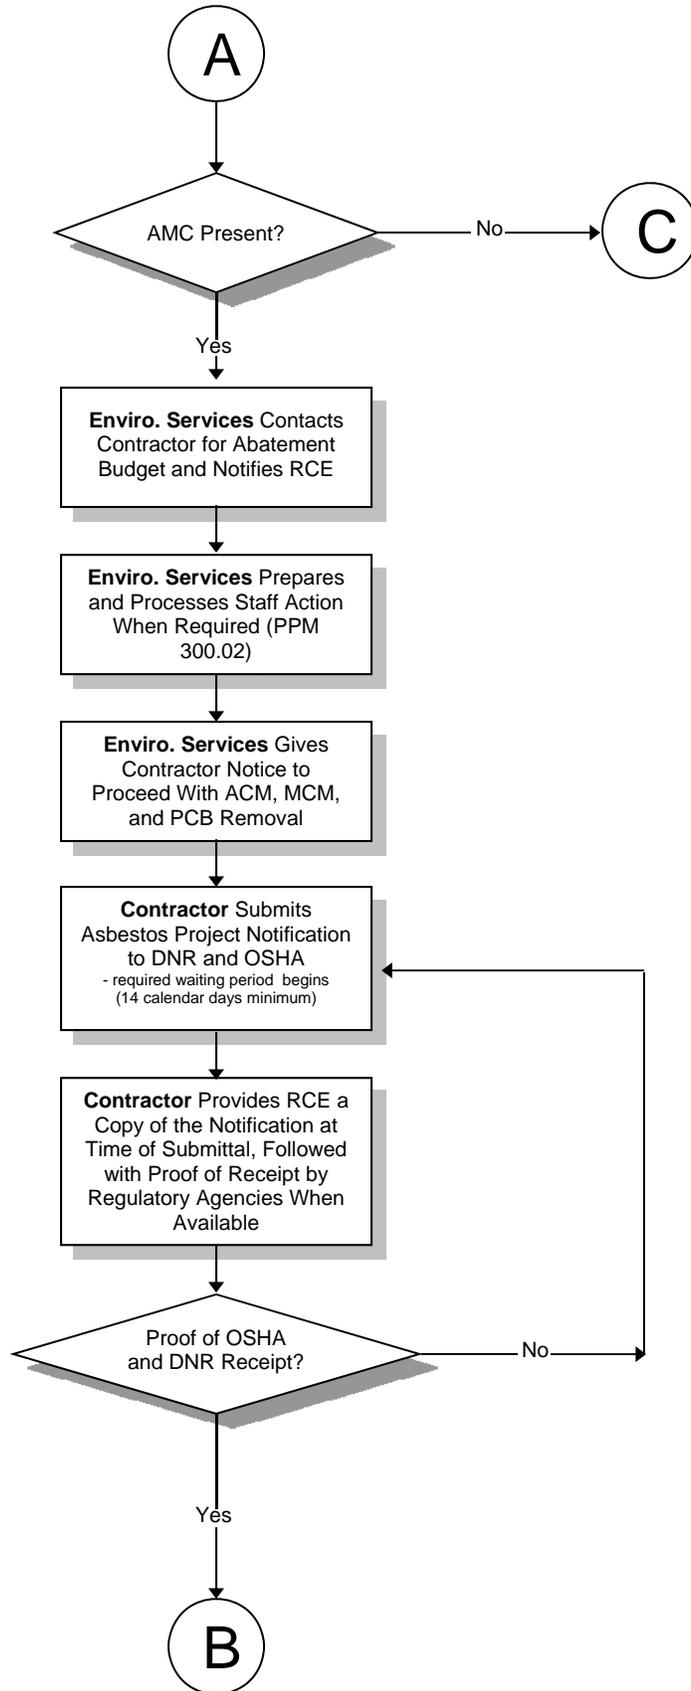

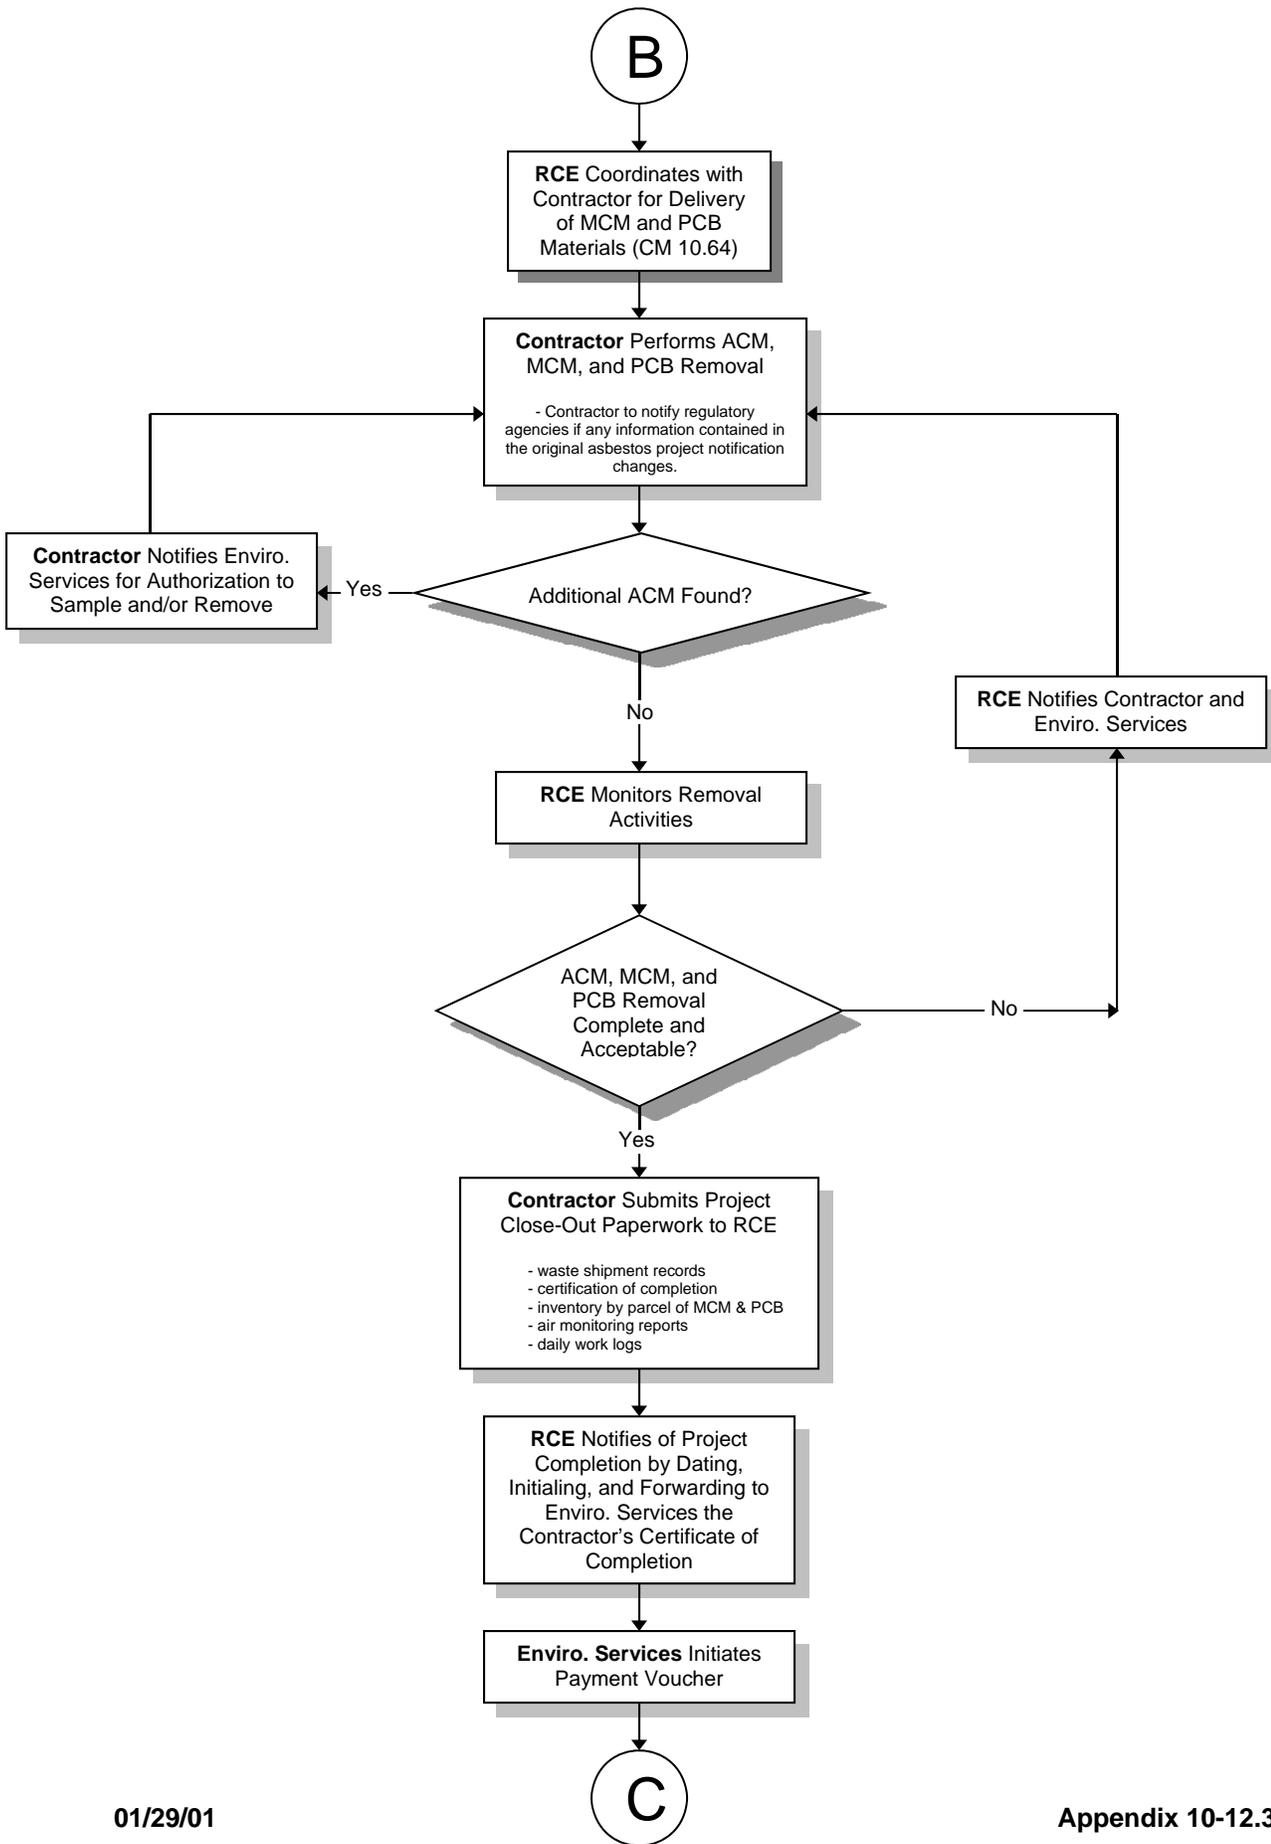

C

Letting of Demolition as Separate Project or Included in Another Project (i.e. Grading Project)

Contractor Notifies RCE of Scheduled Demolition Start Date at Least 25 Calendar Days in Advance of Building Demolition per Article 2538.02 (Div. II)

RCE Notifies Enviro. Services at Least 18 Calendar Days in Advance of Building Demolition by Providing the Information Listed in CM 10.61

Enviro. Services Submits Demolition Notification to DNR at Least 14 Calendar Days in Advance of Building Demolition

Enviro. Services Sends a Copy of the Notification to RCE (Earliest Start Date Listed in Block IX)

Demolition Delayed?*

Yes

Contractor Notifies RCE and Enviro. Services of New Start Date As Soon As Possible, But No Later Than 3 Calendar Days Prior to Original Scheduled Start Date

Enviro. Services Notifies DNR of Demolition Start Date Change per 40 CFR 61.145(b)(3)(iv)(A)

No

Contractor Performs Demolition

RCE Performs Normal Contract Administration

*Due to regulatory requirements, demolition activities cannot begin prior to the originally scheduled start date unless notification can be provided to DNR at least 14 calendar days prior to the new start date [40 CFR 61.145(b)(3)(iv)(B)]
